


Smart Water Utility Solutions- Mueller Mi.Net

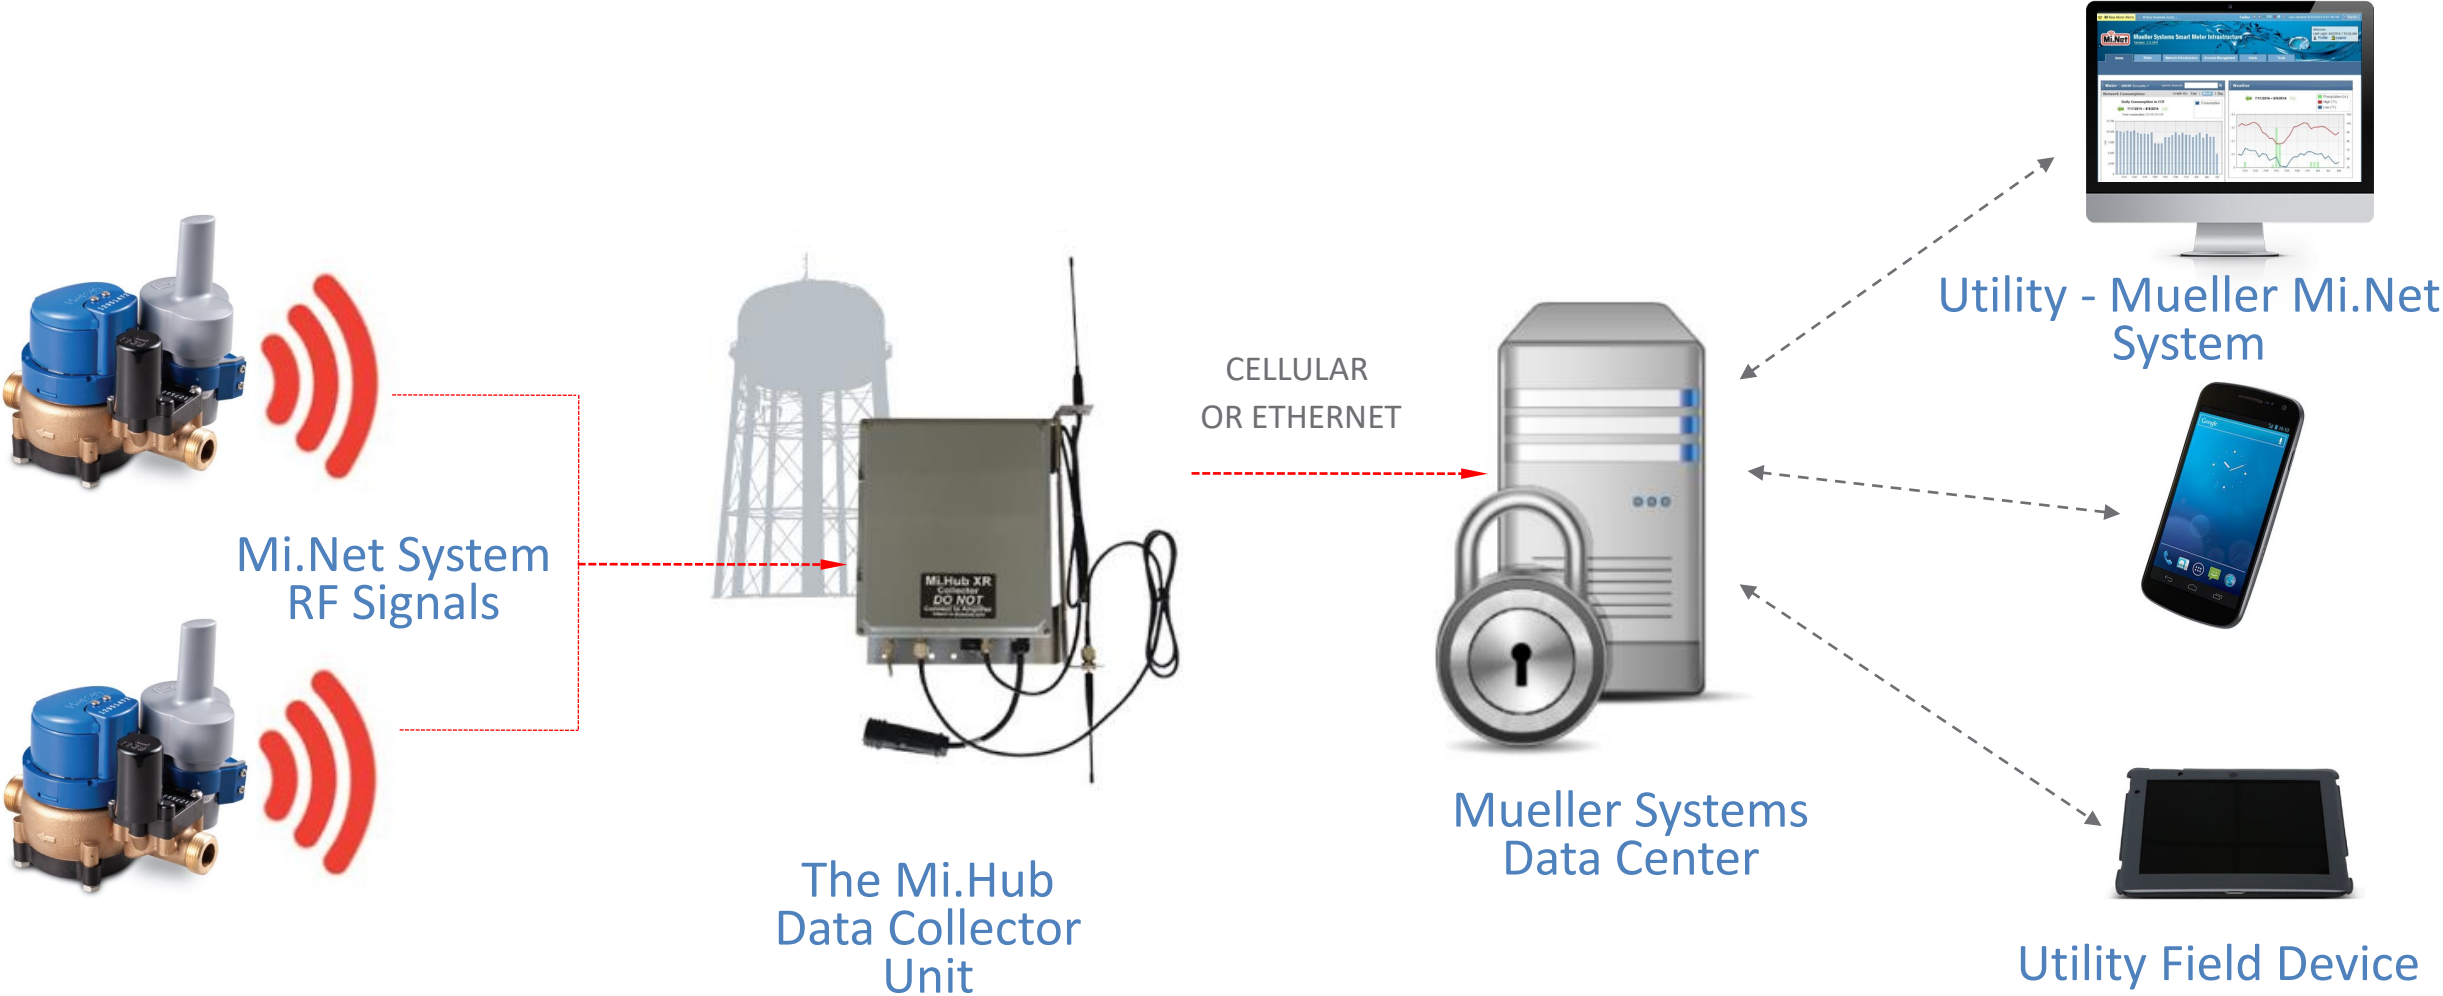

Project Scope and Timeline

PROJECT SETUP & INITIATION: 2/11/20-3/13/20

Coordination of Program Management Elements, Team Assignments, Logistics, Equipment Order, Communications Planning, Integration Planning

AMI NETWORK INSTALLATION AND TESTING: 2/19/20-5/29/20

Preparation of Network Infrastructure (Installation and Connectivity), Hub Installation, RF Sweep

SYSTEMS TESTING AND LIMITED INSTALLATION: 3/4/20-5/8/20

Installation Field Data Management Testing, Large Meter and Special Account Installation, Network Performance Testing, Installation Planning by Route, Preliminary Training, Quality Controls

FULL DEPLOYMENT: 5/11/20-7/31/20

Non-Standard Installation Management, Inventory Controls, Job Aides Development, Customer Portal Activation

PROJECT CLOSEOUT: 8/1/20

Punch-list and Cleanup, Financial Reconciliation, Grant Compliance Validation, RMA Process Management

Network Design Planning and Installation

- Network Design Guarantee
 - 2 MNC Collectors
 - 14 DCXR Repeaters
 - 1 Owned Assets
 - 15 New Locations
- TTLA Utilization

